


CEDAR CREEK TRAIL UPDATE

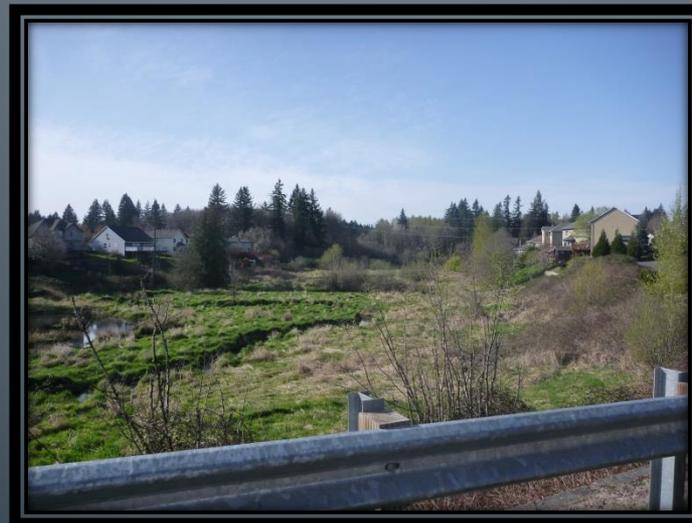

Parks Advisory
Board
October 3 , 2016

Cedar Creek Trail Update

- Cedar Creek Trail Project Overview
- Project 1 Design and Construction
- Project 2 Alignment Design
- Looking Forward



Cedar Creek Trail Project



Decision-Making Structure



Project 1 Preliminary Design

99W to Murdock Road




Trail Facility Types

Shared Use Paths (adjacent to roadways)




Old Town through Stella Olsen Park

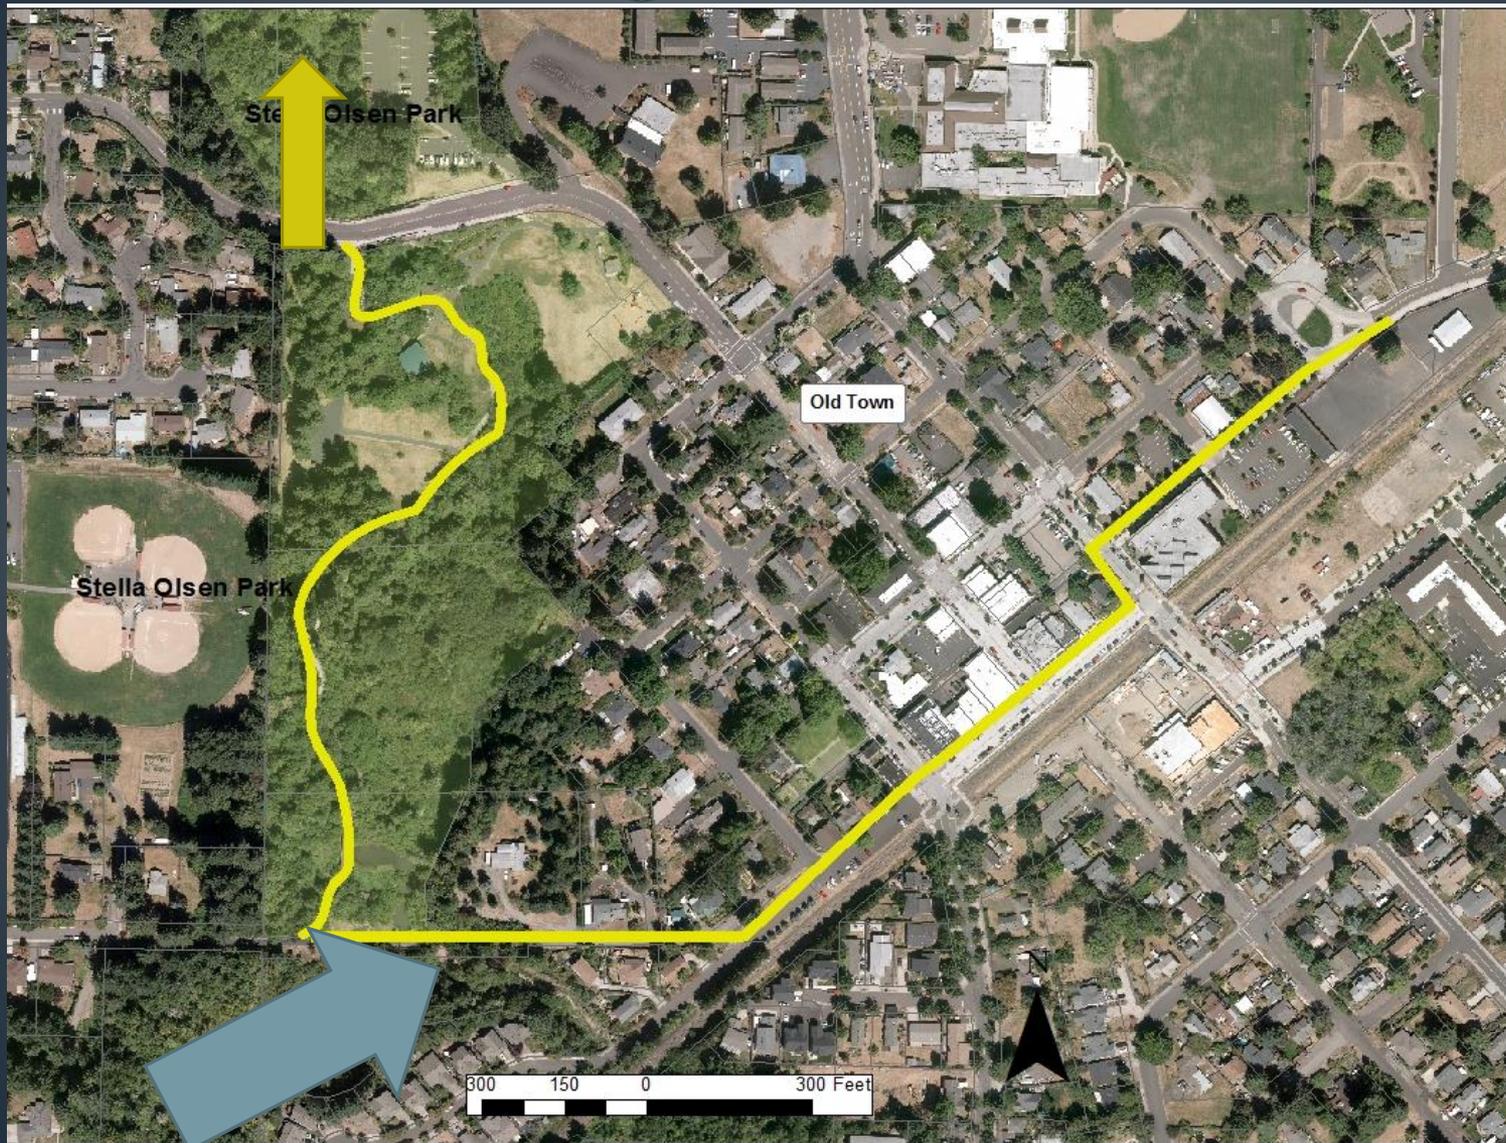

Villa Road



Project 1 Segment from Washington St. Parking Lot to 99W

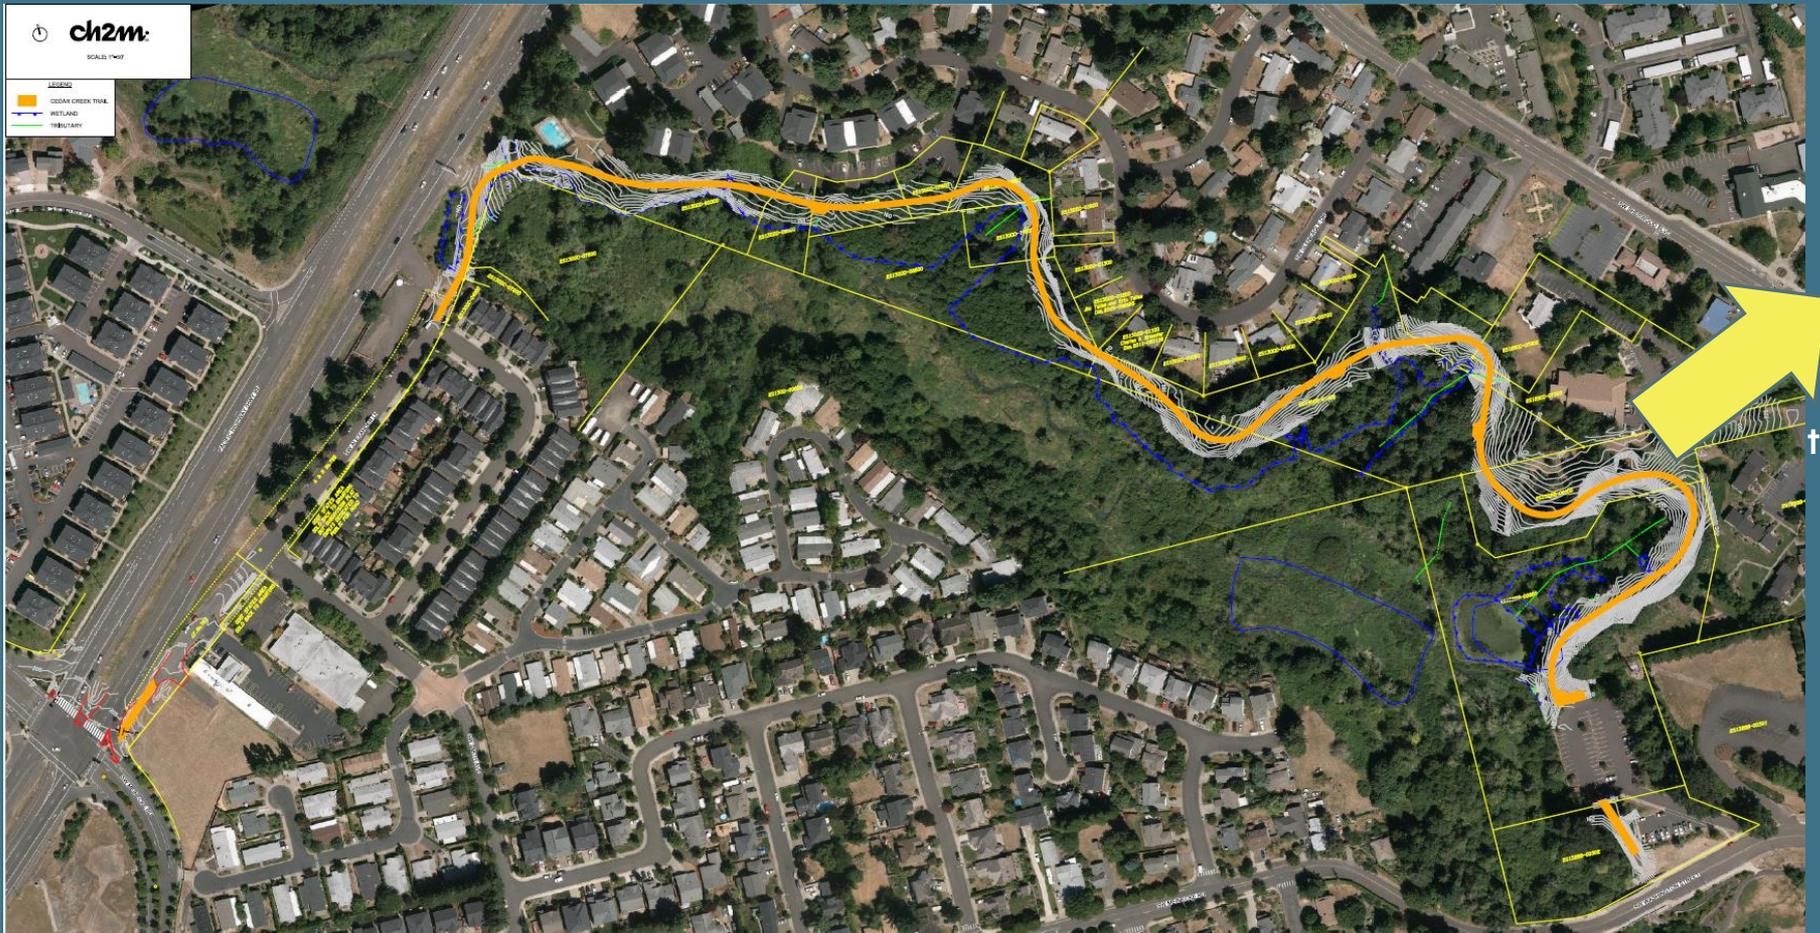



Trail to Washington Street Parking



Trail Facility Types

Shared Use Paths



Project 1 Segment from Washington St. Parking Lot to 99W


Feeder trail to schools



Tualatin Greenway Bridge



99W and Meinecke Intersection Improvements

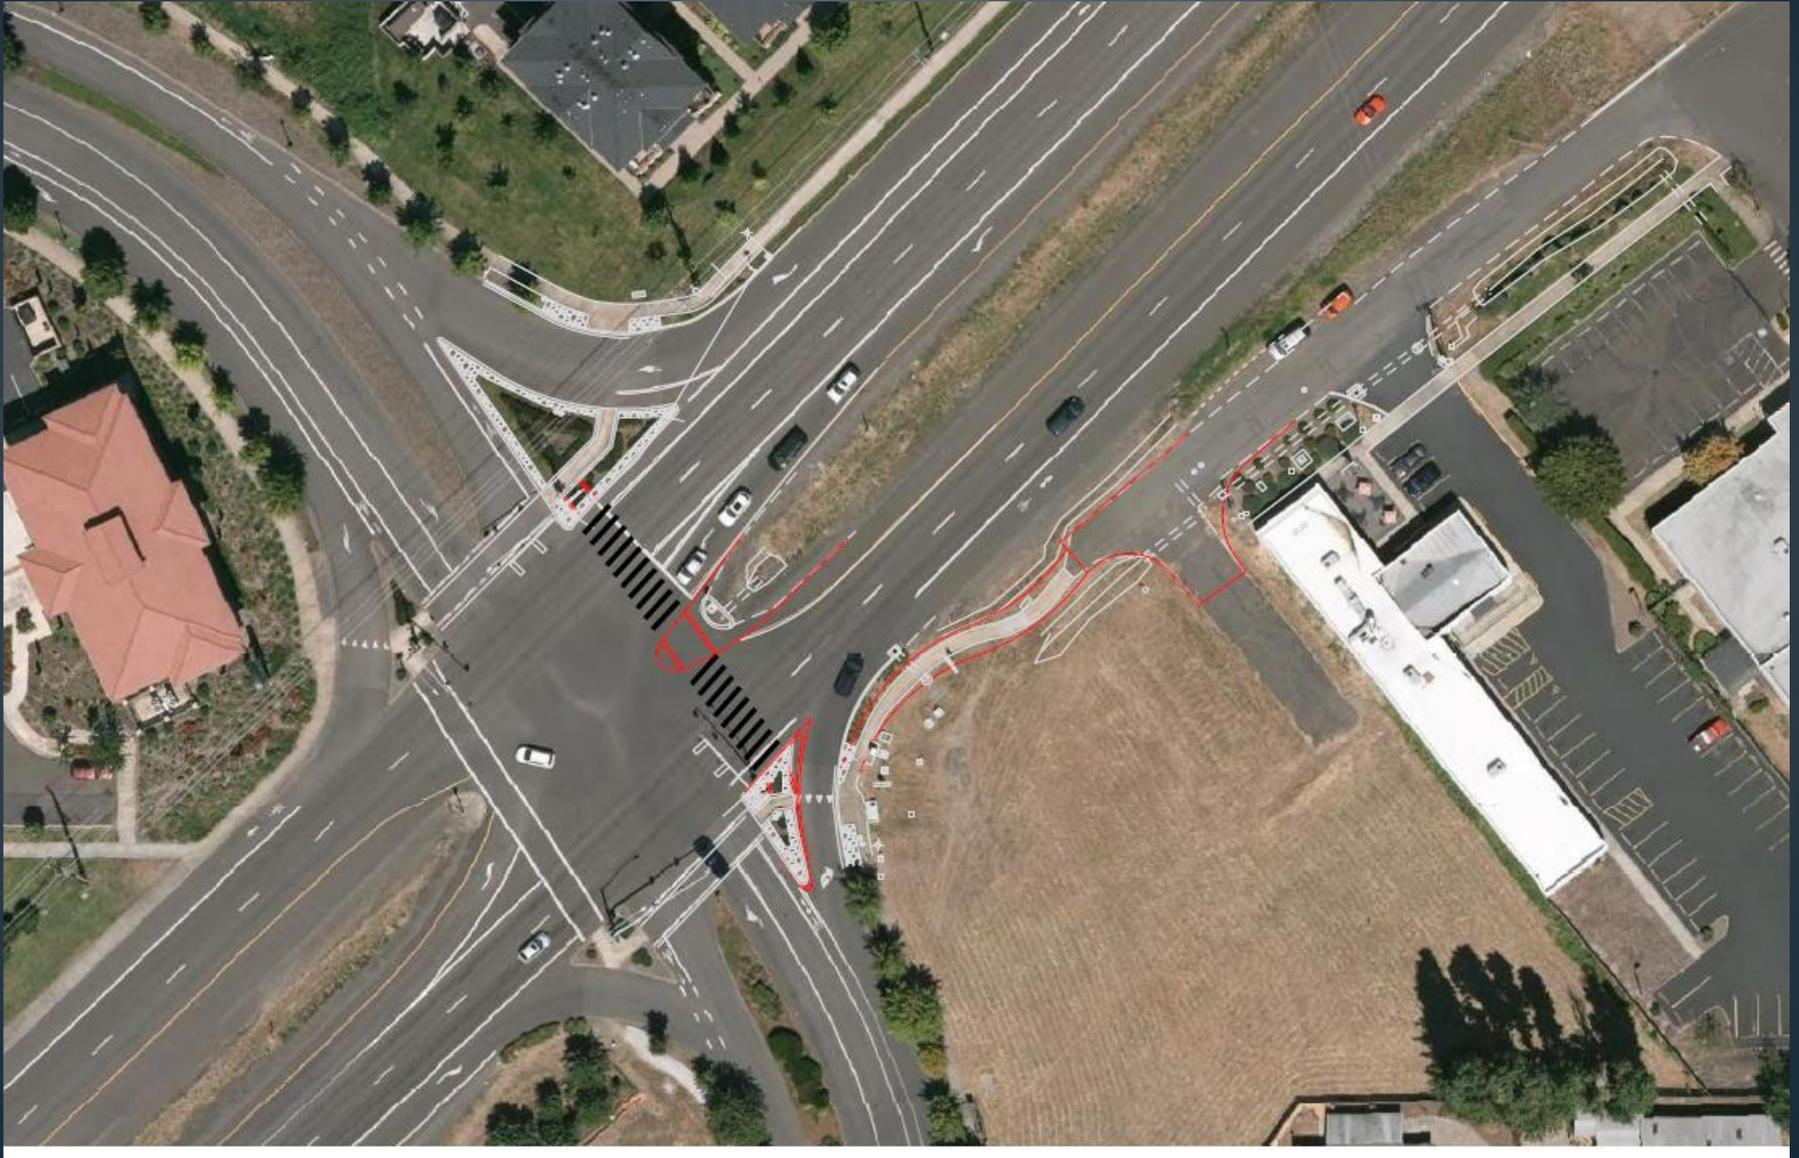


Task	Days	Start	End
30 % Design ODOT and City Review	15	Aug 2, 2016	Aug. 22, 2016- Completed
60 % Design by CH2m	53	Aug. 23, 2016	Oct 27, 2016
60 % Design ODOT and City Review	15	Oct 28, 2016	Nov. 18, 2016
90% Design by CH2M	45	Nov 19, 2016	Jan. 20, 2017
90 % City and ODOT Review	20	Jan 21, 2017	Feb 17, 2017
100 % Submittal	35	Feb 18, 2017	April 7, 2017


Project 2 Preliminary Design

Highway 99W to SW Roy Rogers
Road

Project 2: Miller's Landing and Crossing

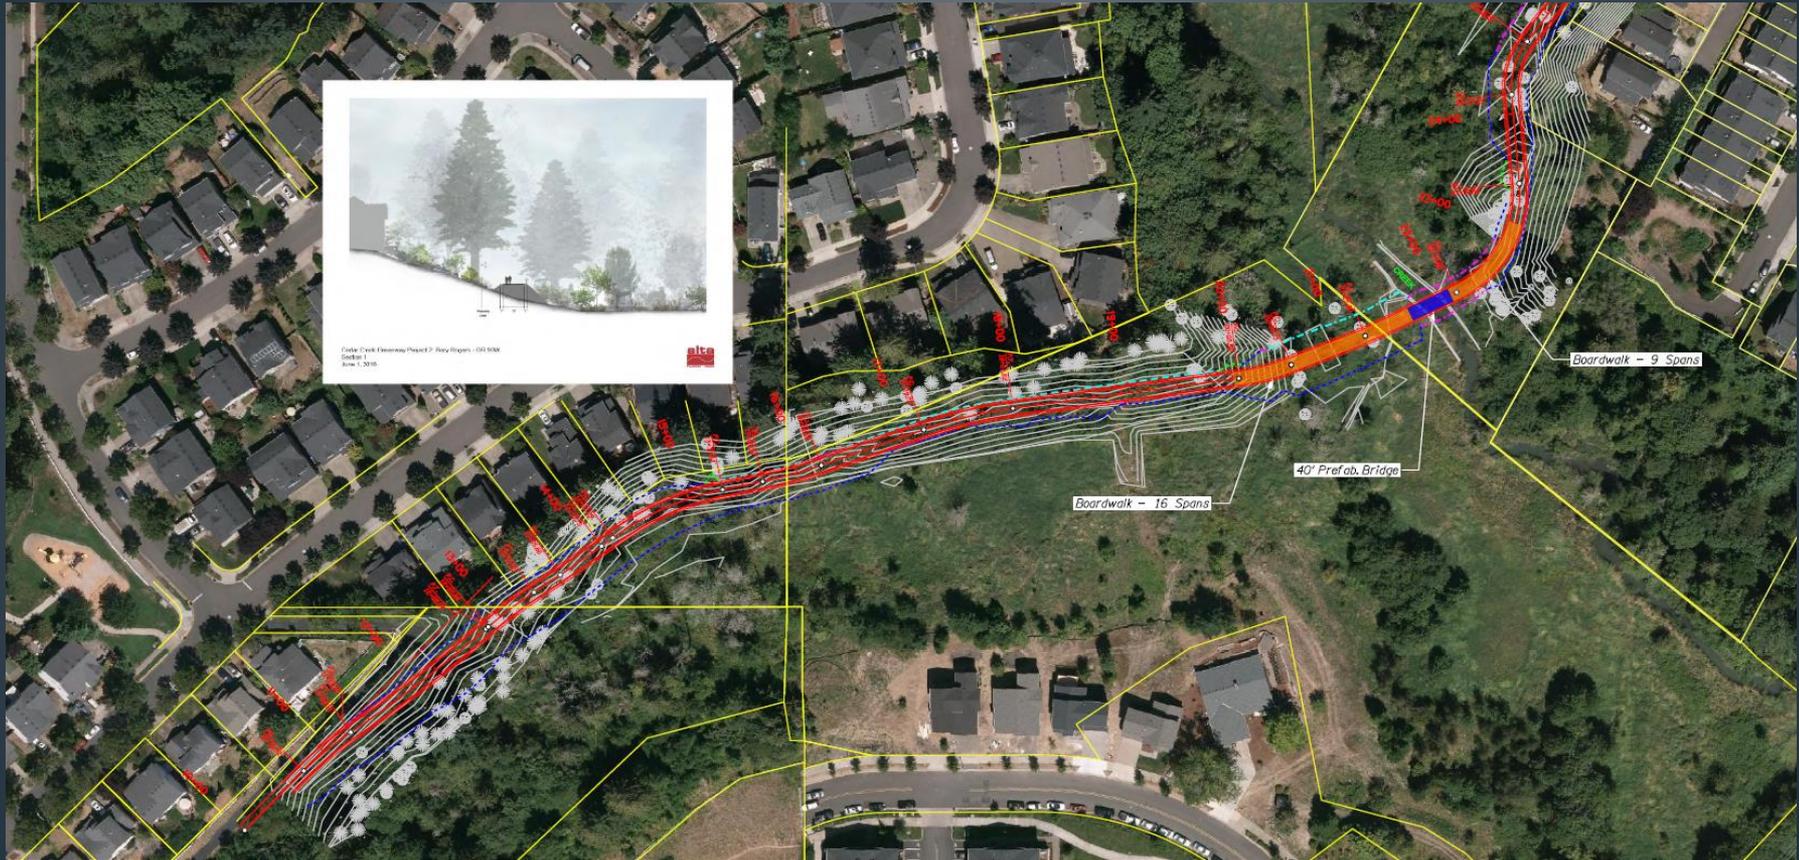

Edy Road

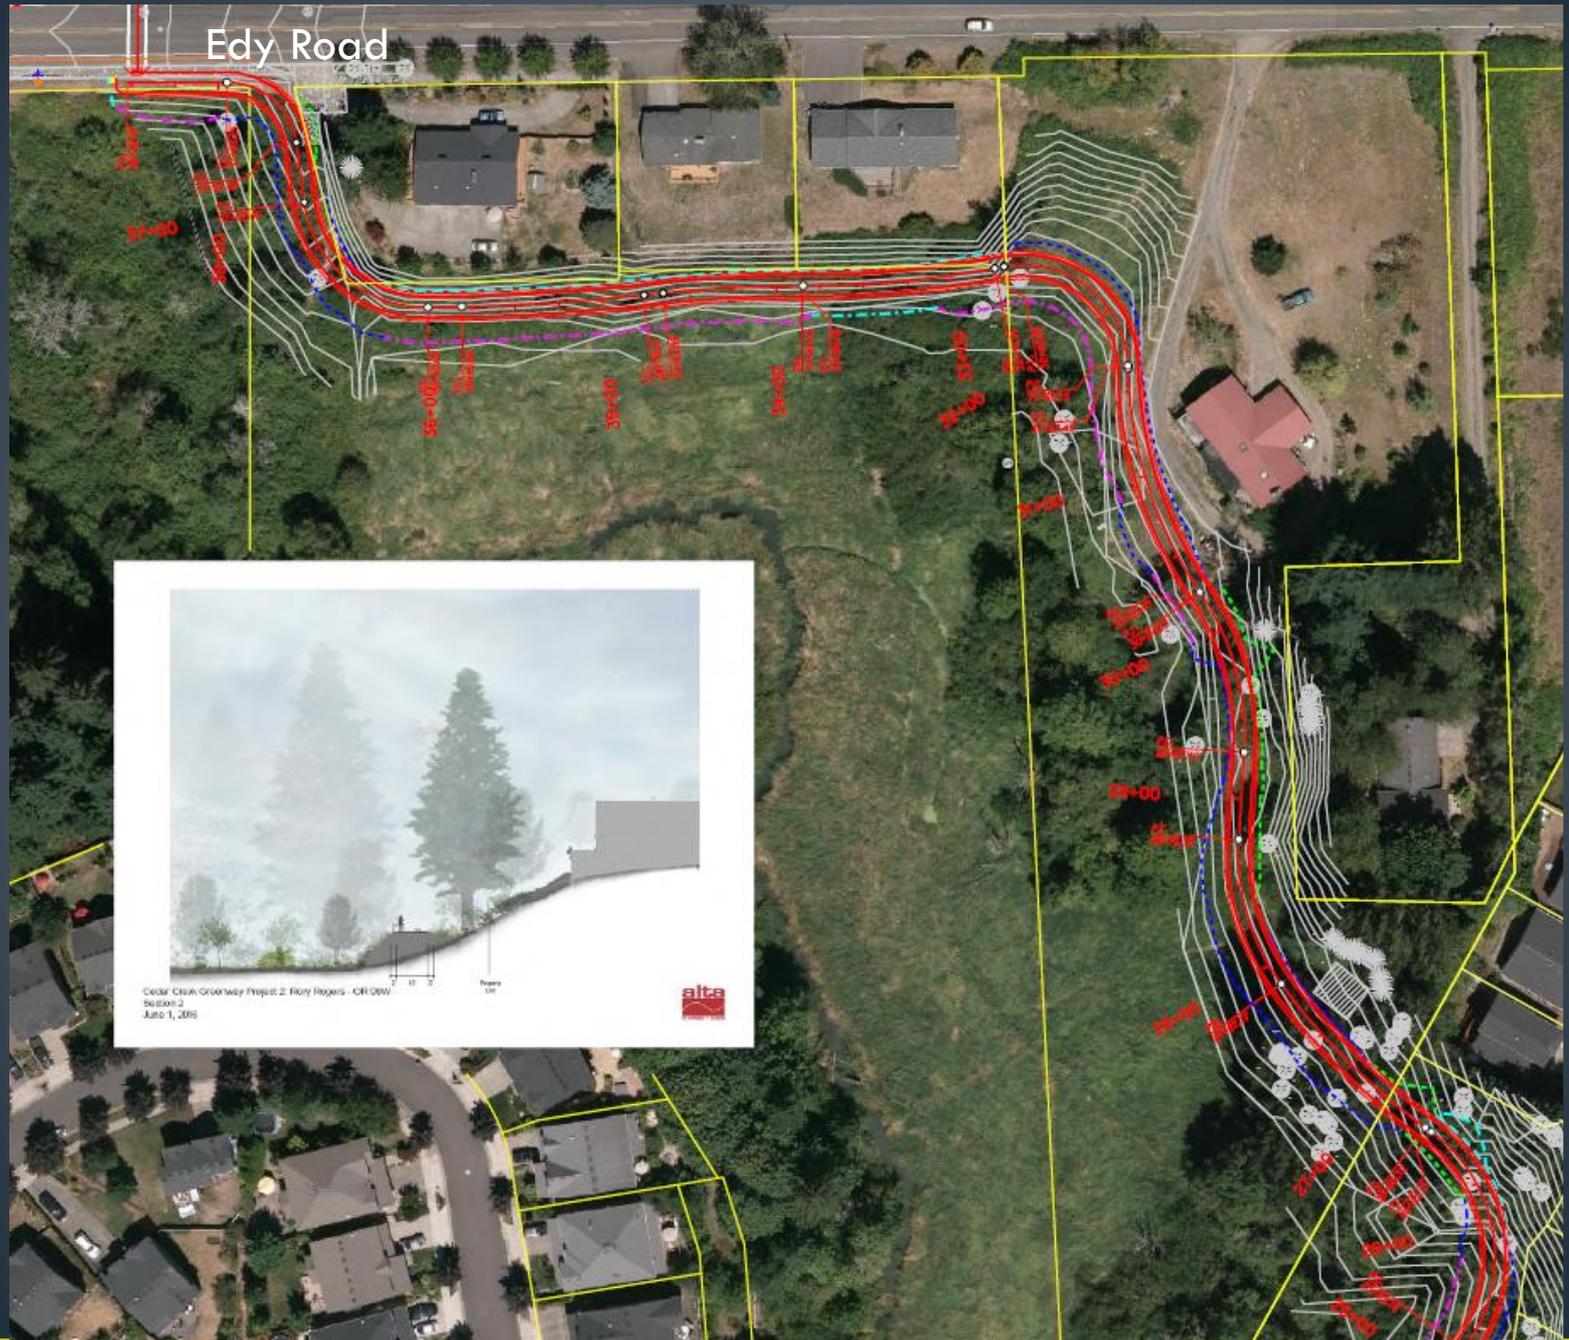

Project 2: Trailblazer



Project 2: North End

Recommended
Alignment




SEGMENT	Construction Estimate
99W NORTH TO Edy Road	\$ 2.45 M
Edy Road to Roy Rogers RD	\$ 3.5 M
GRAND TOTAL (1 MILE OF TRAIL)	<u>\$ 6 M</u>

Next Steps and Schedule

Project 1

- Responding to ODOT Comments
- Engineering Design will be completed early 2017
- **Right of Way – ODOT releases after respond to comments.**
- **Construction begins in 2017-9 month process**



Questions?
